ID	Task Mode	Task Name	Duration	Start	Finish
1		**Resource Consent**	**262 days**	**Mon 11/05/26**	**Tue 11/05/27**
2		Supporting Docs	100 days	Mon 11/05/26	Fri 25/09/26
3		Consent lodged	1 day	Mon 28/09/26	Mon 28/09/26
4		Statutory Stand Down	20 days	Tue 29/09/26	Mon 26/10/26
5		Consent Processing	20 days	Tue 27/10/26	Mon 23/11/26
6		Notification Allowance	160 days	Tue 29/09/26	Mon 10/05/27
7		RFI allowance	15 days	Tue 24/11/26	Mon 14/12/26
8		Consent Granted	1 day	Tue 11/05/27	Tue 11/05/27
9		**EPA**	**76 days**	Wed 14/04/27	Wed 28/07/27
10		Engineering docs	40 days	Wed 14/04/27	Tue 8/06/27
11		Additional Geotech	40 days	Wed 14/04/27	Tue 8/06/27
12		Additional Consultant Input	30 days	Wed 14/04/27	Tue 25/05/27
13		EPA package lodged	20 days	Wed 9/06/27	Tue 6/07/27
14		RFI allowance	15 days	Wed 7/07/27	Tue 27/07/27
15		EPA granted	1 day	Wed 28/07/27	Wed 28/07/27
16		**Contract and Procurement**	**78 days**	**Wed 9/06/27**	**Fri 24/09/27**
17		Contract and supporting docs prepared	15 days	Thu 15/07/27	Wed 4/08/27
18		Initial docs to tenderers	1 day	Wed 9/06/27	Wed 9/06/27
19		Formal Tender period begins	20 days	Thu 5/08/27	Wed 1/09/27
20		Tender Closes	1 day	Thu 2/09/27	Thu 2/09/27
21		Tender Evaluation	5 days	Fri 3/09/27	Thu 9/09/27
22		Negotitation with preferred	5 days	Fri 10/09/27	Thu 16/09/27
23		Tender Accepted	1 day	Fri 17/09/27	Fri 17/09/27
24		Contract Signed	5 days	Mon 20/09/27	Fri 24/09/27
25		**Construction**	**2940 days**	**Fri 1/10/27**	**Fri 7/01/39**
26		**Civils - Main Works**	**480 days**	**Fri 1/10/27**	**Fri 3/08/29**
27		Site Handover Meeting	0 days	Fri 1/10/27	Fri 1/10/27
28		Site Establishment Period	10 days	Mon 4/10/27	Fri 15/10/27
29		Construction	430 days	Mon 18/10/27	Fri 8/06/29
30		Defecting	40 days	Mon 11/06/29	Fri 3/08/29
31		**Vertical Construction**	**2500 days**	**Mon 11/06/29**	**Fri 7/01/39**
32		Staged commercial and residential	2500 days	Mon 11/06/29	Fri 7/01/39

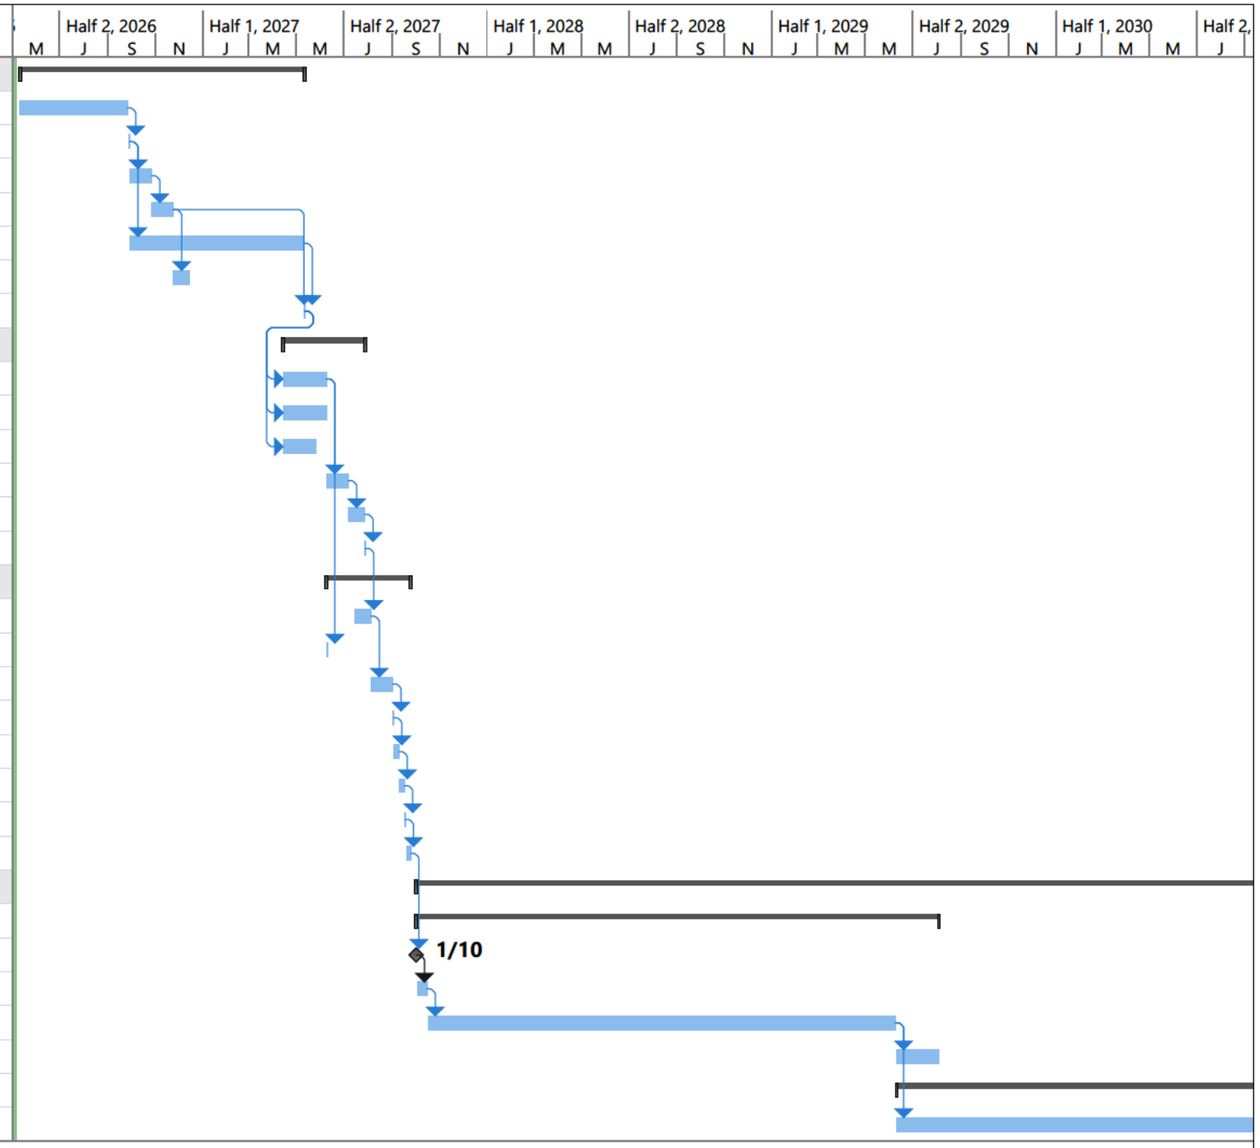

Project: Kapiti Road Programm
Date: Tue 5/05/26

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
